UPLANDS CONSTRUCTION SERVICES

Wimbledon Scout Hut

UPLANDS CONSTRUCTION SERVICES
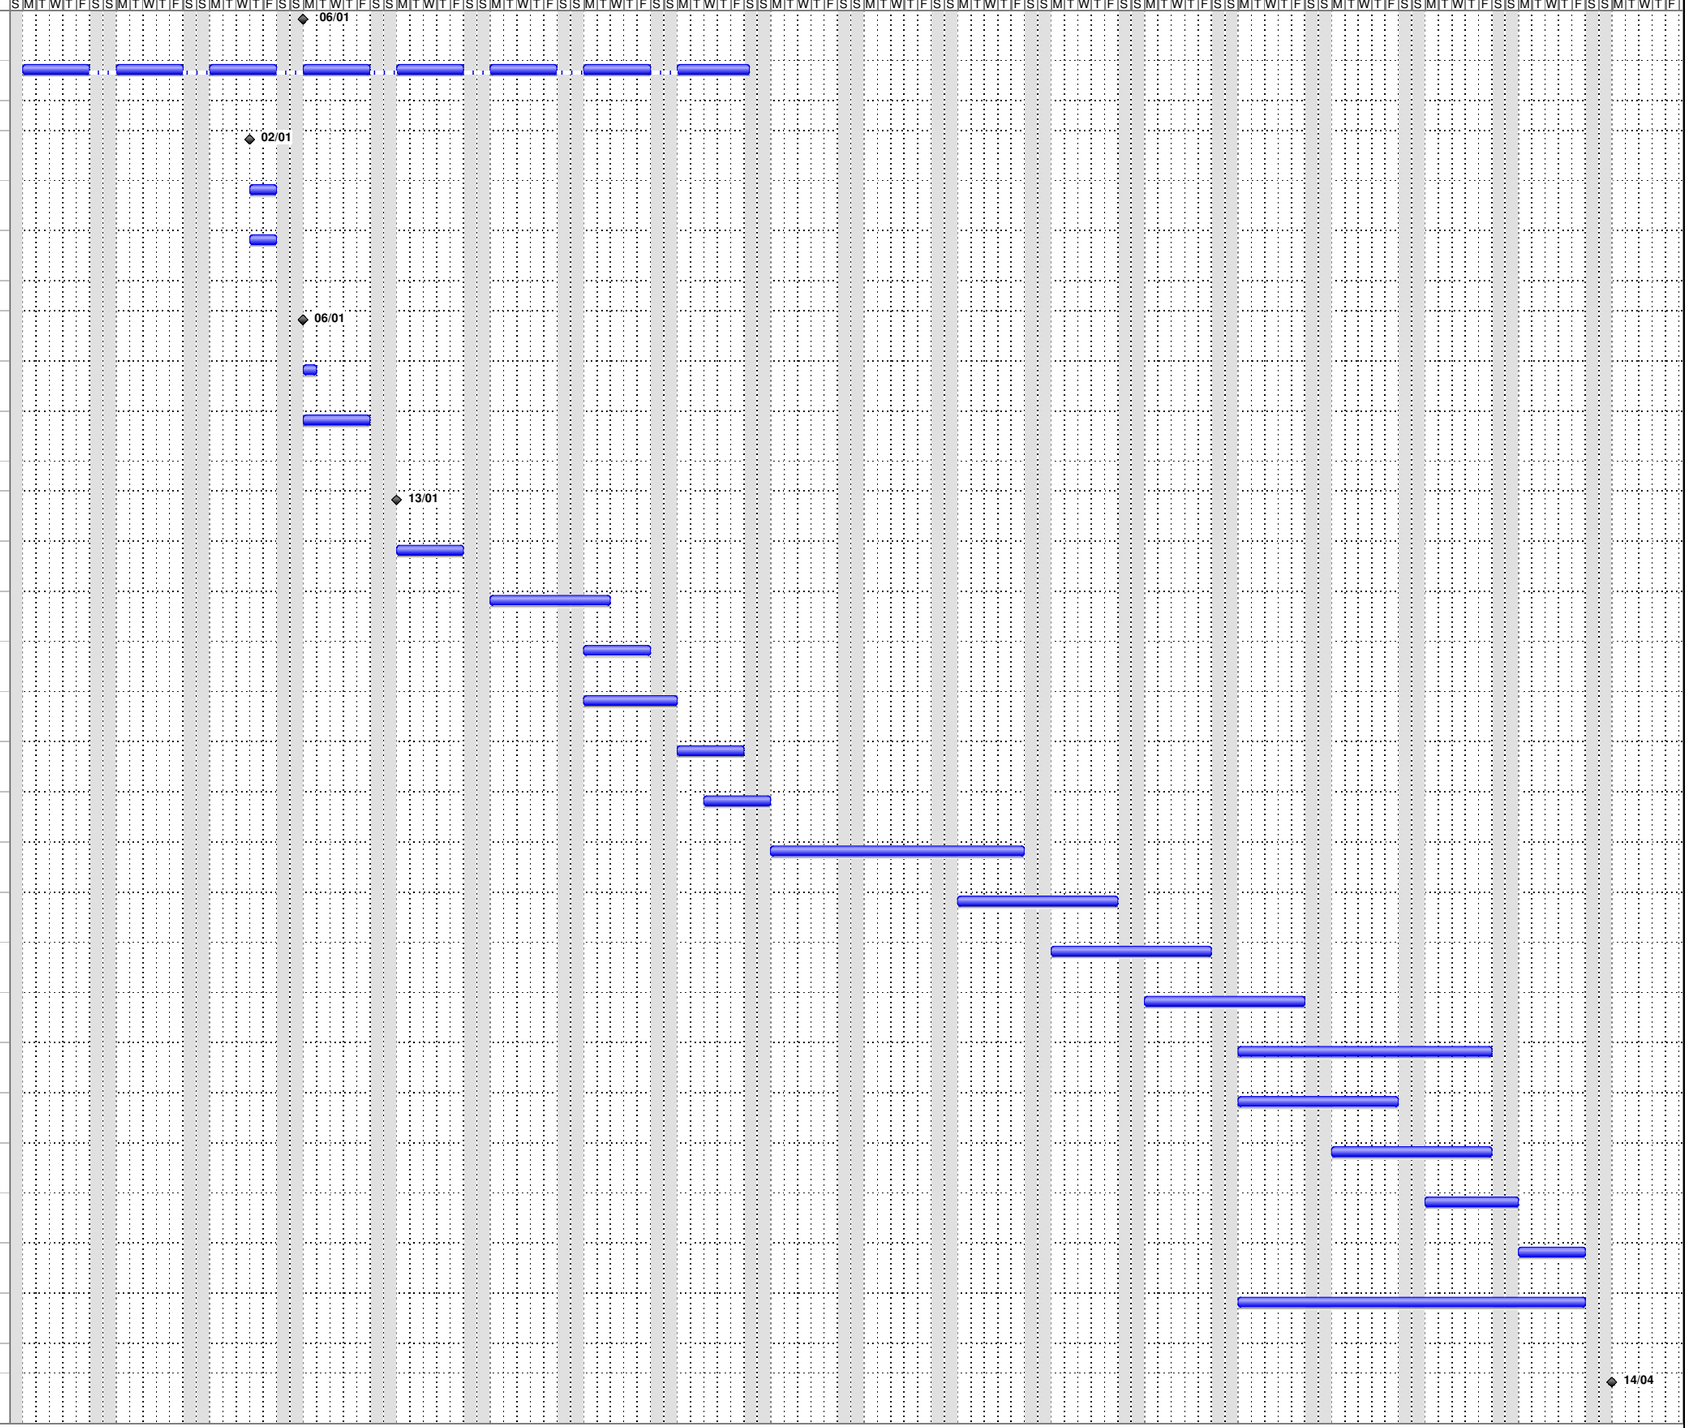
ID	Task Name	Duration	Start
1	**DESIGN / PERIOD**	0 days	Mon 06/01/14
2	Timber frame building / sub.to arch. Design.	36 days	Mon 16/12/13
3			
4	**SITE SET UP**	0 days	Thu 02/01/14
5	Install 2m security fence	2 days	Thu 02/01/14
6	Install site cabins	2 days	Thu 02/01/14
7			
8	**DEMOLITION**	0 days	Mon 06/01/14
9	Make safe M&E	1 day?	Mon 06/01/14
10	Demolish existing hut	5 days	Mon 06/01/14
11			
12	**CONSTRUCTION**	0 days	Mon 13/01/14
13	Reduce level dig	5 days	Mon 13/01/14
14	Form foundations	9 days	Mon 20/01/14
15	Drainage works	5 days	Mon 27/01/14
16	Construct masonry to DPC	7 days	Mon 27/01/14
17	Cast floor slab / services	5 days	Mon 03/02/14
18	Install scaffold to roof level	5 days	Wed 05/02/14
19	Construct building / roof panels	19 days	Mon 10/02/14
20	1st Fix joinery (stud walls / frames)	12 days	Mon 24/02/14
21	External doors / frames	12 days	Mon 03/03/14
22	Timber cladding	12 days	Mon 10/03/14
23	M&E installation	19 days	Mon 17/03/14
24	2nd fix Joinery	12 days	Mon 17/03/14
25	Decorations	12 days	Mon 24/03/14
26	Floor coverings	7 days	Mon 31/03/14
27	Fit out	5 days	Mon 07/04/14
28	External works	26 days	Mon 17/03/14
29			
30	**HANDOVER**	0 days	Mon 14/04/14
